CONST. NO. 51005-3230-14

PROJECT NO.	YEAR	SHEET NO.
NH-99(51)	2015	

REVISIONS

NO.	DATE	BY	BRIEF DESCRIPTION

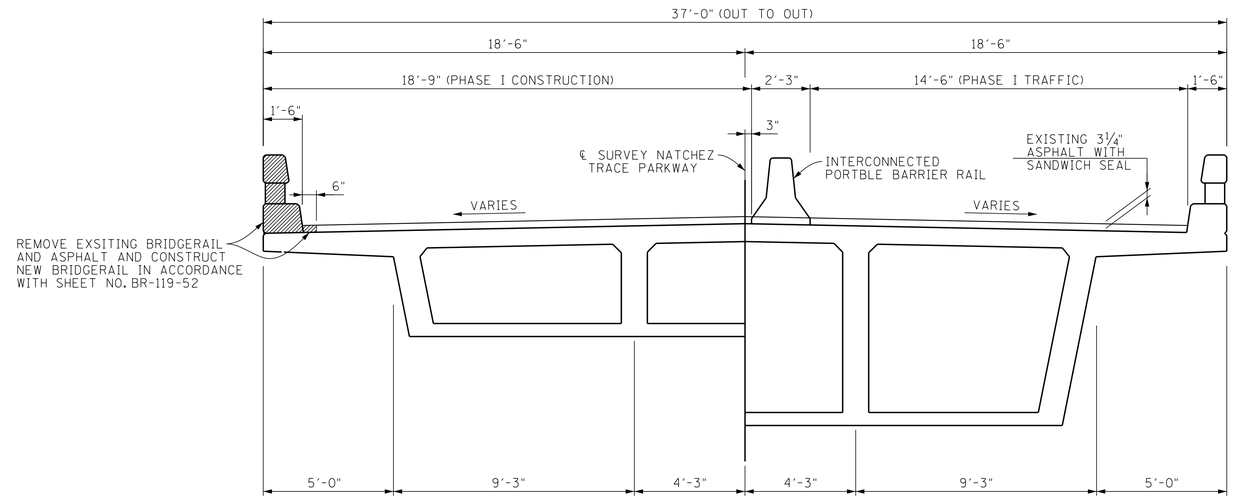

PHASE I CONSTRUCTION
(LOOKING FORWARD ON SURVEY)

DENOTES: EXISTNG CONCRETE TO BE REMOVED ITEM NO. 202-04.01 (TYP.)

PHASE I CONSTRUCTION

1. REMOVE EXISTING BRIDGERAIL AND CONSTRUCT NEW RAIL. SEE SHEETS NO. BR-119-52 AND BR-119-53 FOR RAIL CONSTRUCTION SEQUENCE.
2. REPLACE PORTION OF ABUTMENT AT ABUTMENT NO. 1 AND ABUTMENT NO. 2. SEE SHEET NO. BR-119-54 FOR DETAILS.
3. REPLACE ASPHALT TO PROVIDE TEMPORARY DRIVING SURFACE FOR PHASE II TRAFFIC.

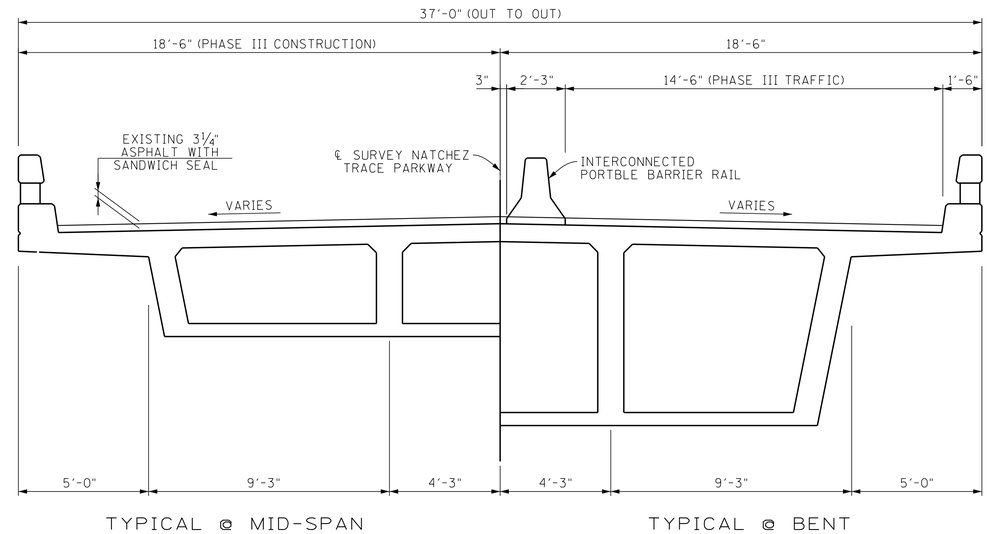

PHASE III CONSTRUCTION
(LOOKING FORWARD ON SURVEY)

PHASE III CONSTRUCTION

1. REMOVE ASPHALT OVERLAY AND SEAL.
2. SEAL COLD JOINT AND TEMPORARY ACCESS OPENING. SEE DETAILS ON. SHEET NO. BR-119-54.
3. PLACE SEAL AND ASPHALT IN ACCORDANCE WITH SHEET NO. BR-119-50.
4. PLACE EXPANSION JOINTS AT ABUTMENT NO. 1 AND NO. 2 AND JOINTS AT END OF APPROACH PAVEMENT.

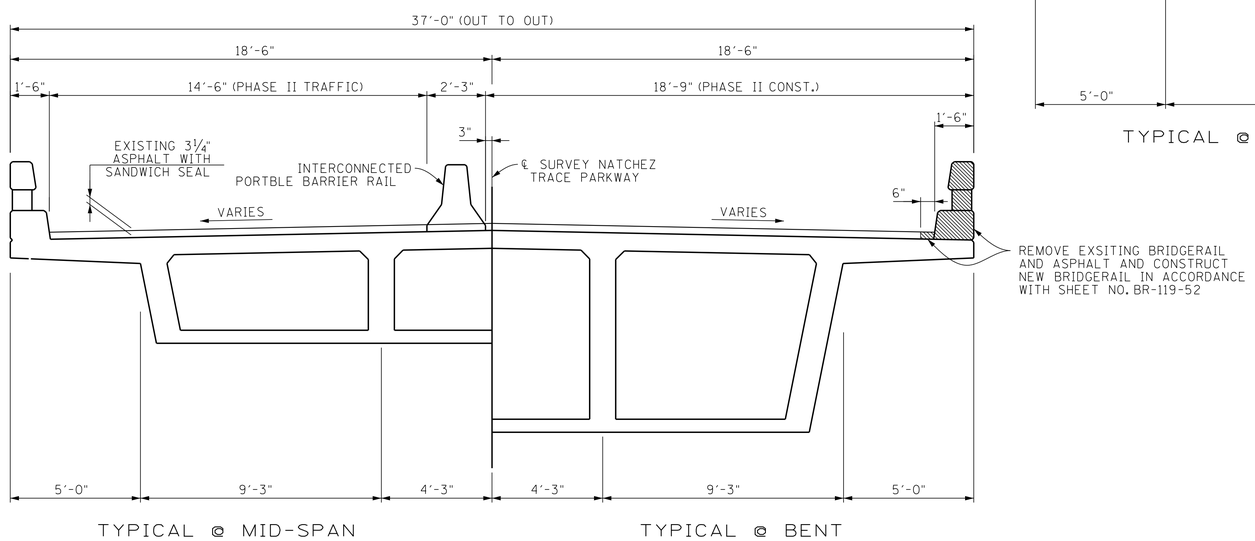

PHASE II CONSTRUCTION
(LOOKING FORWARD ON SURVEY)

DENOTES: EXISTNG CONCRETE TO BE REMOVED ITEM NO. 202-04.01 (TYP.)

PHASE II CONSTRUCTION

1. REMOVE EXISTING BRIDGERAIL AND CONSTRUCT NEW RAIL. SEE SHEETS NO. BR-119-52 AND BR-119-53 FOR RAIL CONSTRUCTION SEQUENCE.
2. REPLACE PORTION OF ABUTMENT AT ABUTMENT NO. 1 AND ABUTMENT NO. 2. SEE SHEET NO. BR-119-54 FOR DETAILS.
3. REMOVE ASPHALT OVERLAY AND SEAL.
4. SEAL COLD JOINT AND TEMPORARY ACCESS OPENING. SEE DETAILS ON. SHEET NO. BR-119-54.
5. PLACE SEAL AND ASPHALT IN ACCORADANCE WITH SHEET NO. BR-119-50.

JOHN S. HASTINGS
STATE OF TENNESSEE
06/01/2015

STATE OF TENNESSEE
DEPARTMENT OF TRANSPORTATION
PHASE CONSTRUCTION DETAILS
NATCHEZ TRACE PARKWAY
OVER STATE ROUTE 99
STATION 24+93.51
LEWIS COUNTY
2015

CORRECT Wayne G. Sepe
ENGINEER OF STRUCTURES

DESIGNED BY	J.S. HASTINGS	DATE	12-14
DRAWN BY	KEVIN MARTINKO	DATE	3-15
SUPERVISED BY	J.S. HASTINGS	DATE	1-15
CHECKED BY	J.S. HASTINGS	DATE	5-15
